



2025 Santa Cruz Wharf End Interim Repair Project Communications Team Update

Jan. 24, 2026 through Feb.10, 2026




Bents 167-171 Post Collapse



Bents 167-170 End Interim Repair

- 18 total piles driven.
- Rebuild of Bent 170 underway.
- Batter pile driven.
- Engineering inspections of completed and anticipated work conducted.


(see project images following page)

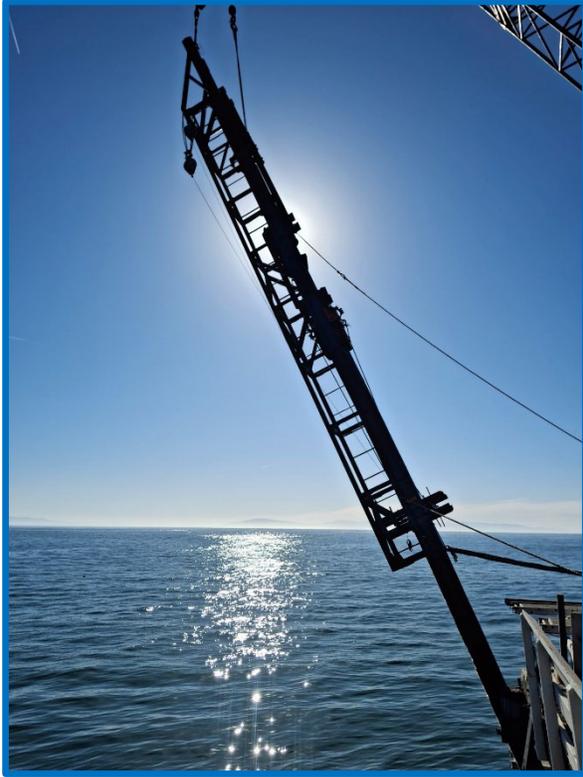

Batter pile poised for driving




First strike of the pile driver hammer

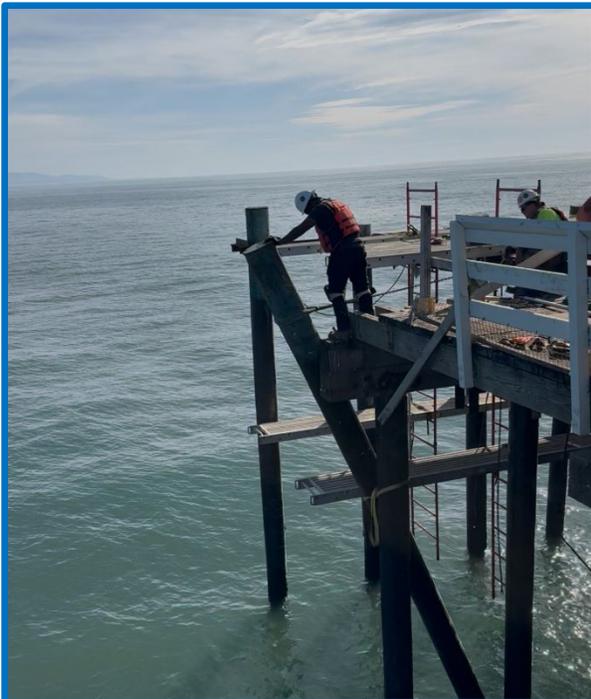

Batter pile in place ready to bolt to plumb pile

Batter piles are driven into the seafloor at a 45 degree angle, and act as a brace against sideways movement of the Wharf caused by wind and waves.

Plumb piles are driven vertically and support the weight of the Wharf structure and buildings.

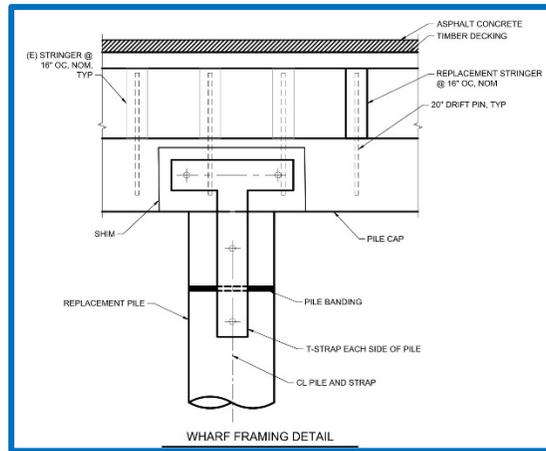

Wharf framing detail

